

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Project Backlog, Sprint Planning, Estimation & Tracking

Date	01 October 2026
Team ID	SWTID-2026-7951
Project Name	Script-Controlled ACL – Restrict Record Access Based on Field Value
Maximum Marks	5 Marks

Project Planning Basis:

The planning is derived directly from the project requirement: a script-controlled ACL must restrict record viewing according to the Branch field, allow EEE users to view EEE records, and preserve full administrator access.

Template alignment:

The supplied planning template requires a Product Backlog/Sprint Schedule with Sprint, Functional Requirement (Epic), User Story Number, User Story/Task, Story Points, Priority and Team Members, followed by a Project Tracker with sprint points, duration, dates, completed points and release date.

1. Product Backlog, Sprint Schedule and Estimation (4 Marks)

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	User & Role Context	USN-1	As a system, I can identify the logged-in user and retrieve the role/branch information required for access evaluation.	3	High	
Sprint-1	User & Role Context	USN-2	As an administrator, I can be identified as an administrator so that the branch restriction does not block my access.	2	High	
Sprint-1	Record Branch Validation	USN-3	As the ACL, I can read the Branch field of the requested record before deciding whether the user can view it.	3	High	
Sprint-2	Script-Controlled ACL	USN-4	As an EEE user, I can view a record when the record's Branch field is EEE.	3	High	

Sprint-2	Script-Controlled ACL	USN-5	As a non-EEE user, I cannot view a record when the record is restricted to EEE.	3	High	
Sprint-2	Administrator Access	USN-6	As an administrator, I can view records across branches without being blocked by the EEE branch condition.	2	High	
Sprint-3	Access Denial & Validation	USN-7	As the system, I deny record access when the user does not satisfy the required branch condition.	2	High	
Sprint-3	Testing & Documentation	USN-8	As a tester, I can verify EEE-user, non-EEE-user and administrator access scenarios.	2	High	
Sprint-3	Testing & Documentation	USN-9	As a developer, I can document the ACL logic and test results for future maintenance.	1	Medium	

21 story points. The workload is divided into three focused sprints so that the access-control foundation is completed before functional restriction testing and final validation.

2. Sprint Goals

Sprint	Sprint Goal	Story Points
Sprint-1 – Access Foundation	Establish user/role context and record Branch validation. Confirm that the ACL has the information needed to make a record-level decision.	8
Sprint-2 – Core ACL Behaviour	Implement the scripted decision: EEE user + Branch = EEE → allow; administrator → allow; unauthorized branch user → deny.	8
Sprint-3 – Validation & Release	Validate all access scenarios, verify denial behaviour, document the implementation and prepare the final release.	5

3. Project Tracker, Velocity & Burndown Chart (4 Marks)

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	8	6 Days	05 Oct 2026	10 Oct 2026	8	10 Oct 2026
Sprint-2	8	6 Days	12 Oct 2026	17 Oct 2026	8	17 Oct 2026
Sprint-3	5	6 Days	19 Oct 2026	24 Oct 2026	5	24 Oct 2026

Velocity:

The template illustrates average velocity as story points completed per sprint duration. For this plan, Sprint-1 has 8 points over 6 days, Sprint-2 has 8 over 6 days, and Sprint-3 has 5 over 6 days. Planned total = 21 points over 18 working days, giving an overall planned average velocity of approximately **21 ÷ 18 = 1.17 story points/day**. The sprint-level velocity is 1.33, 1.33 and 0.83 story points/day respectively.

4. Burndown Chart

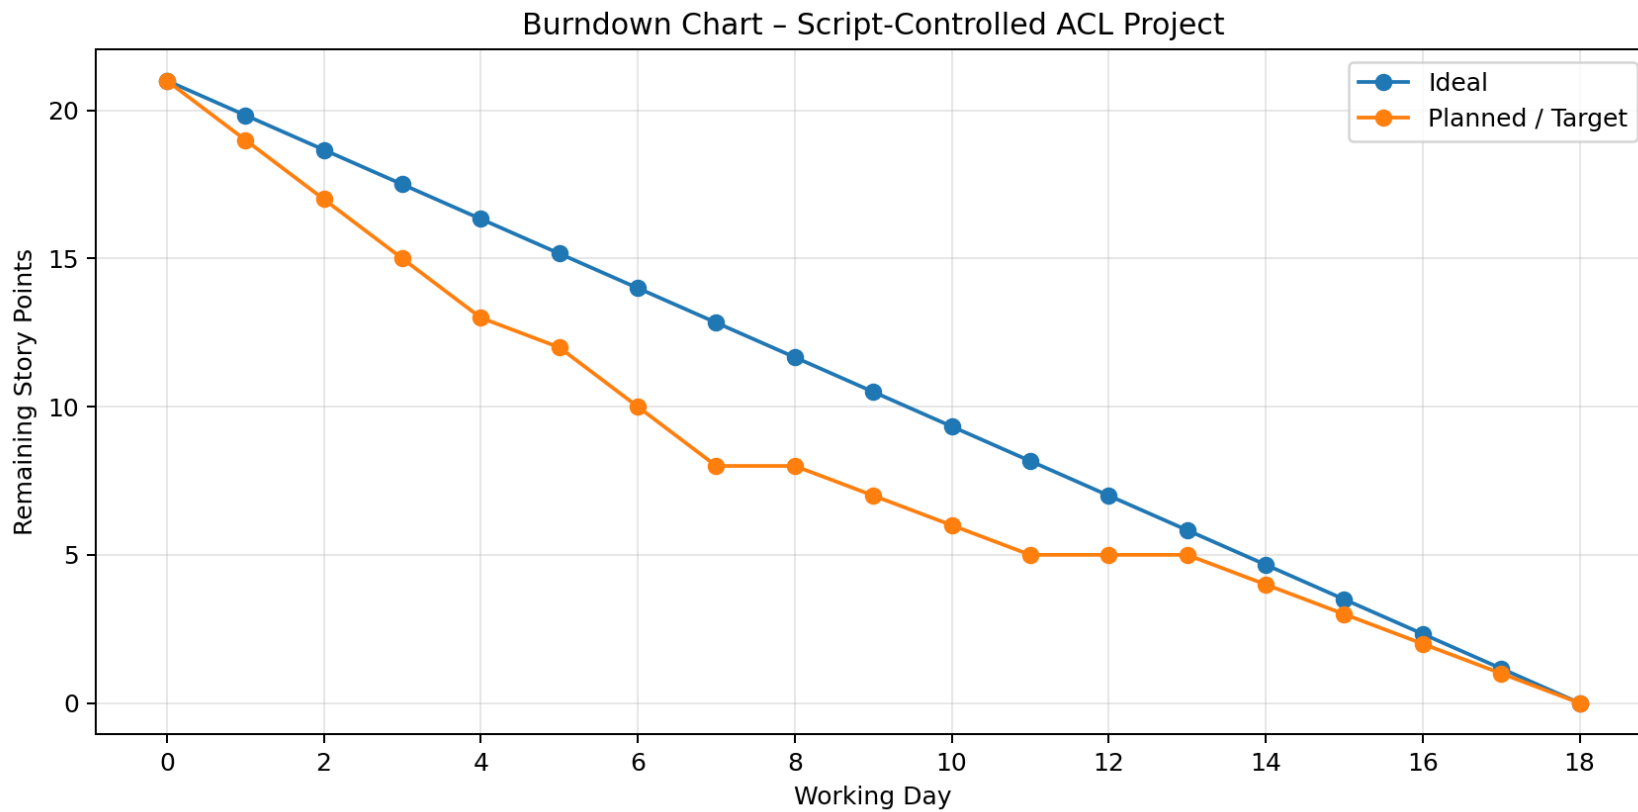


Figure 1: Planned burndown of the 21-story-point project backlog.

5. Sprint Completion / Definition of Done

- The ACL script is configured on the intended record/table access control.
- The logged-in user's role and branch context are correctly available to the authorization logic.
- EEE users can view records where Branch = EEE.
- Users who do not satisfy the required branch condition cannot view the protected EEE records.
- Administrators retain full access across branch values.
- Access-denied behaviour is verified for unauthorized users.
- EEE, non-EEE and administrator test cases are executed and documented.
- The final ACL logic is documented for maintenance and future branch expansion.

Planning note:

The dates above are a proposed academic project schedule based on the current date and the supplied template's sprint-planning structure. Team-member names and actual completion dates can be filled in after the team finalizes responsibilities.
